

Project:

Client:

Building element/floor/room:

Installation company:

Screed layer:

Screed work completed on:

Start of functional heating with 20 °C to 25 °C flow temperature on:

Start of functional heating with maximum 55 °C flow temperature on:

End of functional heating on:

Function heating interrupted? ☐ no ☐ from: to:

Was the heated floor area free? ☐ yes ☐ no


Were the rooms ventilated without draughts? ☐ yes ☐ no

The system was released for further construction work at an outside temperature of °C on:

Client:

Installation company:

Site management/architect:

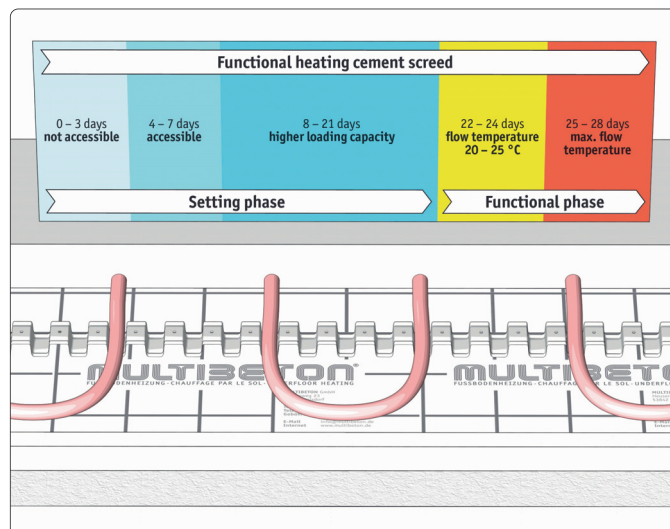

After functional heating, it is not yet ensured that the screed has reached the prescribed residual moisture for the floor covering to be applied.
A Ready-for-laying heating may be necessary.

Project:

Client:

Building element/floor/room:

Installation company:

Screed layer:

Screed work completed on:

Start of functional heating with 20 °C to 25 °C flow temperature on:

Start of functional heating with maximum 55 °C flow temperature on:

End of functional heating on:

Function heating interrupted? ☐ no

☐ from: to:

Was the heated floor area free? ☐ yes

☐ no

Were the rooms ventilated without draughts? ☐ yes


☐ no

The system was released for further construction work at an outside temperature of °C on:

Client:

Installation company:

Site management/architect:

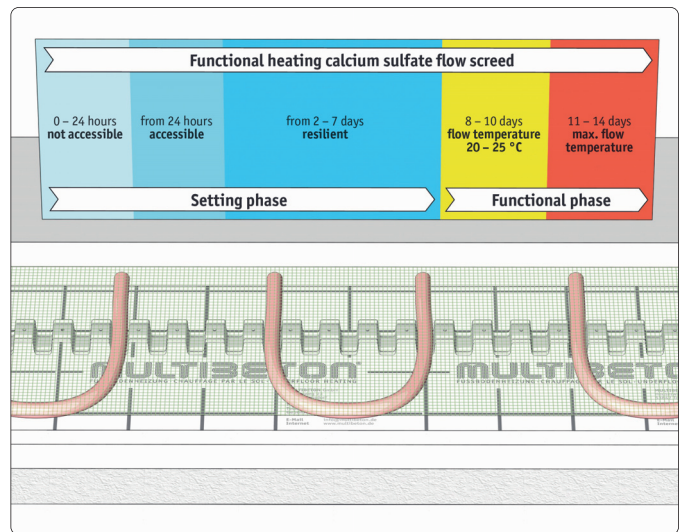

After functional heating, it is not yet ensured that the screed has reached the prescribed residual moisture for the floor covering to be applied.
A Ready-for-laying heating may be necessary.
